

Somerville College The Ratan Tata Building Newsletter Kingerlee




Date: 10th July 2026

Works have continued to progress across the site over the last period. Making-good works have been completed around the newly formed opening in the existing boundary wall, leaving the area clean and tidy.

Debris has been cleared from the site, and preparations have begun for the upcoming drainage and piling works. This includes removing the existing paving along the storm drainage diversion and breaking out the concrete slab within the courtyard area.



The next phase of works will include disconnecting the three existing streetlights, continuing the storm drainage diversion and preparing for the piling mat. Excavations will then be backfilled and levelled in preparation for the upcoming piling works.

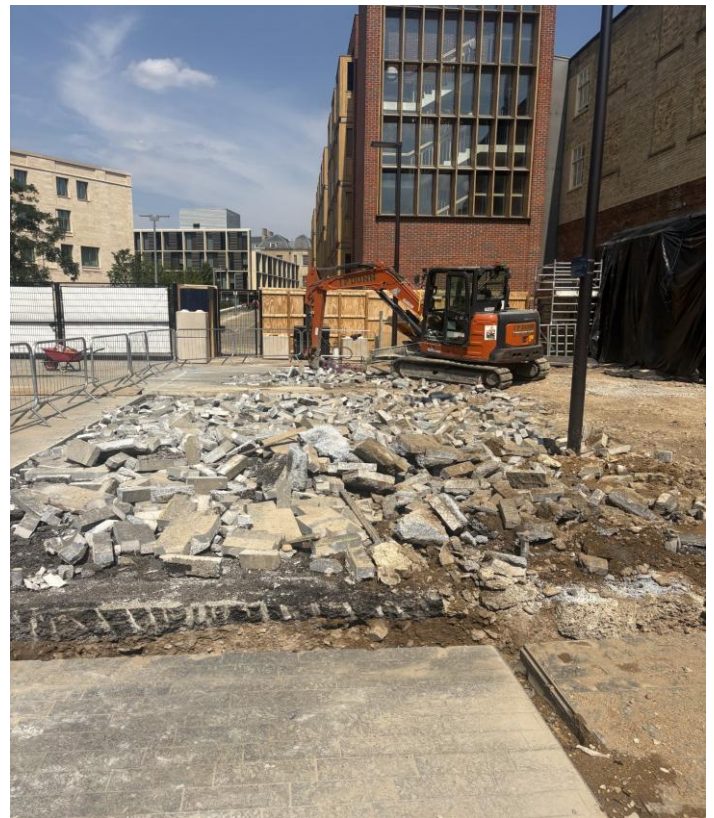

**Early Warnings SSEN Removal of Electric Cable
Provisional Dates 16 – 20th August 2026 Tower
Crane Installation Provisional Dates 1st- 3rd
September 2026**

For any further Information on the Project please
contact Martin Clarke
Tel: 07398 568029
email martin.clarke@kingerlee.co.uk
